




# Ida Street Paving Improvement Project

## UPDATE AS OF JUNE 16TH:

### PROGRESS REPORT:

Pacific Excavation have completed most of the stormwater system improvements for the Ida Street Pavement and Water System Improvements project. The water main will begin to be constructed starting the week of **June 16** and estimated to be completed in two (2) weeks.

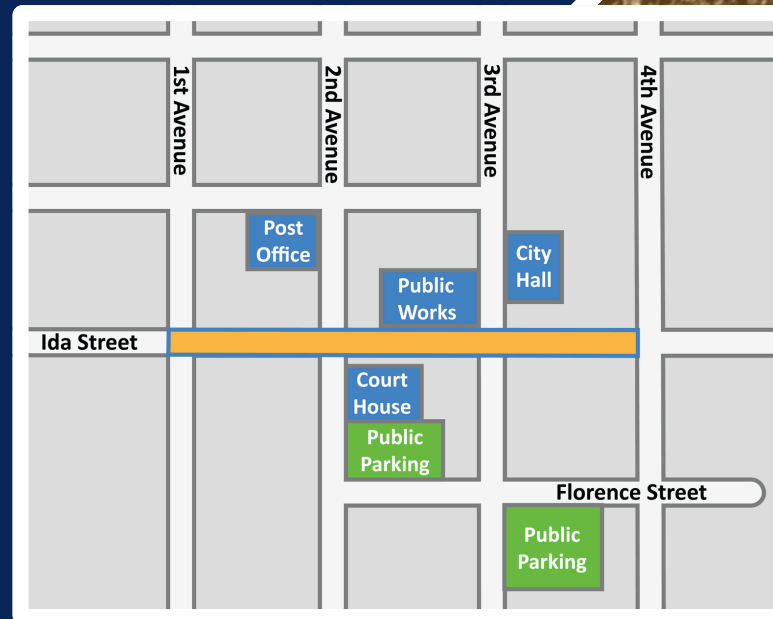

### UPCOMING CONSTRUCTION?

- Pacific Excavation will be working be performing night construction from **10 PM to 6 AM of Ida St. and 1st Ave. from June 16-17.**
- Starting **June 24**, construction will begin on new curbs, sidewalks, and ADA compliant corner ramps. The contractor will work with businesses to allow access during business hours. Notices will be posted via door hanger for any sidewalk closures or water shutdowns.
- **Free public parking** is available on the corner of **Florence St. and 2nd Ave.** and behind the **Stayton Municipal Court.**

Contact **Ian Kintz-Stormo** at **(503) 769-2919**, if you have questions.

Visit our **Projects** page to stay up to date and learn more about our current and upcoming projects. Scan the QR code here - - - >

